

SFDRCISD **FACILITIES &** **CONSTRUCTION** **REPORT**



Project Status: May 21, 2018

Operations @ A Glance

New Construction

- Laughlin Campus
- Stadium Guest Bleachers
- Portable Buildings

Technology Department

- Monthly Service Requests

Maintenance Department

- Austin Campus Renovations
- Monthly Service Requests

New Construction

Laughlin Elementary STEM Magnet School



- ✓ Arrival of first modular - 2-16-18
- ✓ Set crew arrives to join buildings - 2-23-18
- ✓ Set crew finishes - 3-15-18
- ✓ Technology Cable Installation – In Progress
- ✓ Parking Lot – 4-1-18
- ✓ Floor Waxing – 5-1-18
- ✓ Furniture Delivery – 5-7-18
- ✓ Walkways - 5-15-18
- ✓ Fire & Security finished - 5-15-18
- Interior work, data intercom - 5-25-18
- Food Service Equipment Delivery 5-25-18
- Hosting Day Camp – July 17th , 18th , 19th

New Construction

Walter Levermann Ram Stadium – Bleachers



- ✓ Board Approved – 1/22/2018
- ✓ Demo of Bleachers - Scheduled – 2/12/2018 – Delayed (Rescheduled to 2/19/2018)
- ✓ Schematic Drawings of Storage, Restrooms, and Concession Stand – March 2018 – 1st Review



- ✓ Foundation Fill – 4/16/18
- ✓ Cement Footing Installation – 4/24/18
- ✓ Bleacher Installation – 5/10/2018
- ✓ Schematic Drawings of Storage, Restrooms, and Concession Stand – 6/18/18 – 2nd Review

New Construction

Surplus Portable Buildings



- ✓ 3/9/2018 – Establish Moving Options
- ✓ 3/25/2018 – Publish Portables – News Herald
- ✓ 4/3/2018 – Site Visits – Completed
- ✓ 5/1/2018 – Begin Contacting Interested Parties
- ✓ 6/1/2018 – Proceed with Scheduled “Pickups”

Hosted Onsite Visits


- Public = 1
- Private = 5
- Individual = 9

Formal Commitments Received

- Public = 1
- Private = 2
- Individual = 2

Technology Department – Monthly Service Requests

Support Tickets 4-1-2018 thru 5-1-2018

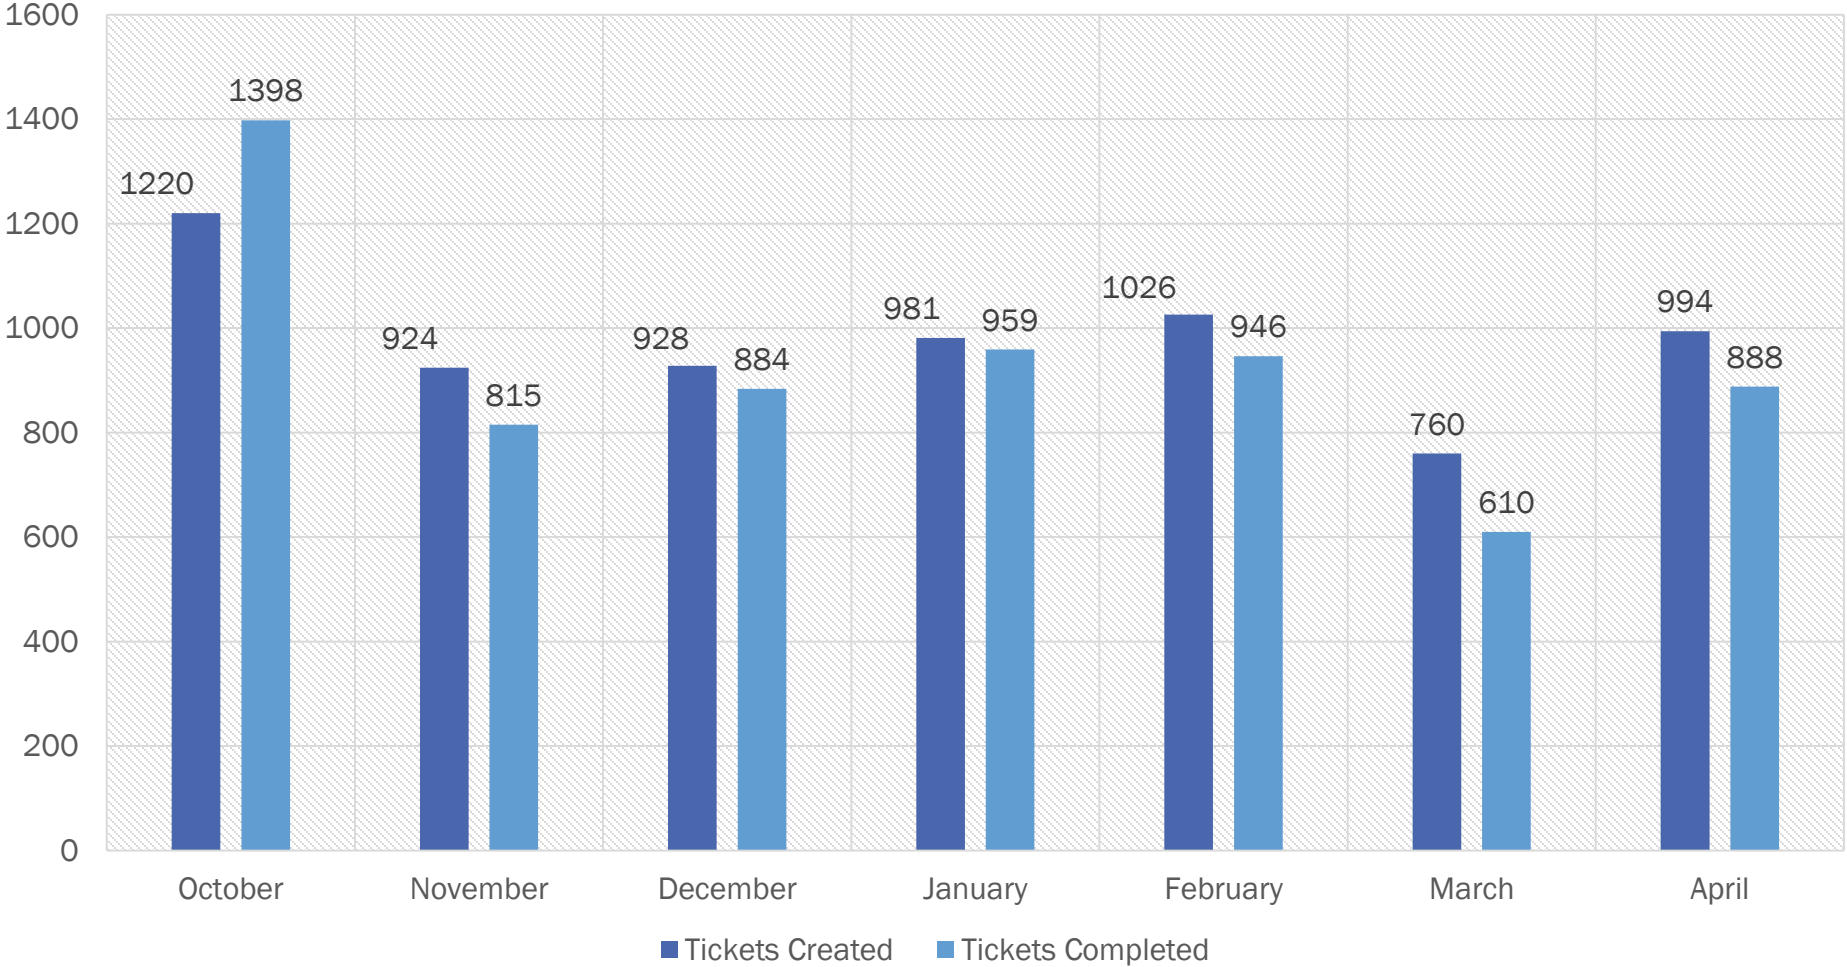

Created = 994
Closed = 888
Within 30 Days = 106
60 Days = 1
90 + Days = 0

Maintenance Department

Austin Campus – Renovations

MAINTENANCE DEPARTMENT



Maintenance Move

- Electricians – Completed
- Painters – Completed
- HVAC – Completed
- Carpentry – Completed
- Plumbing – In Progress

TECHNOLOGY DEPARTMENT




Technology Move

- Technology Office – In Progress
- District Call Center – In Progress
- Staff Move – In Progress

Maintenance Department – Monthly Service Requests

Support Tickets 4-1-2018 thru 5-1-2018

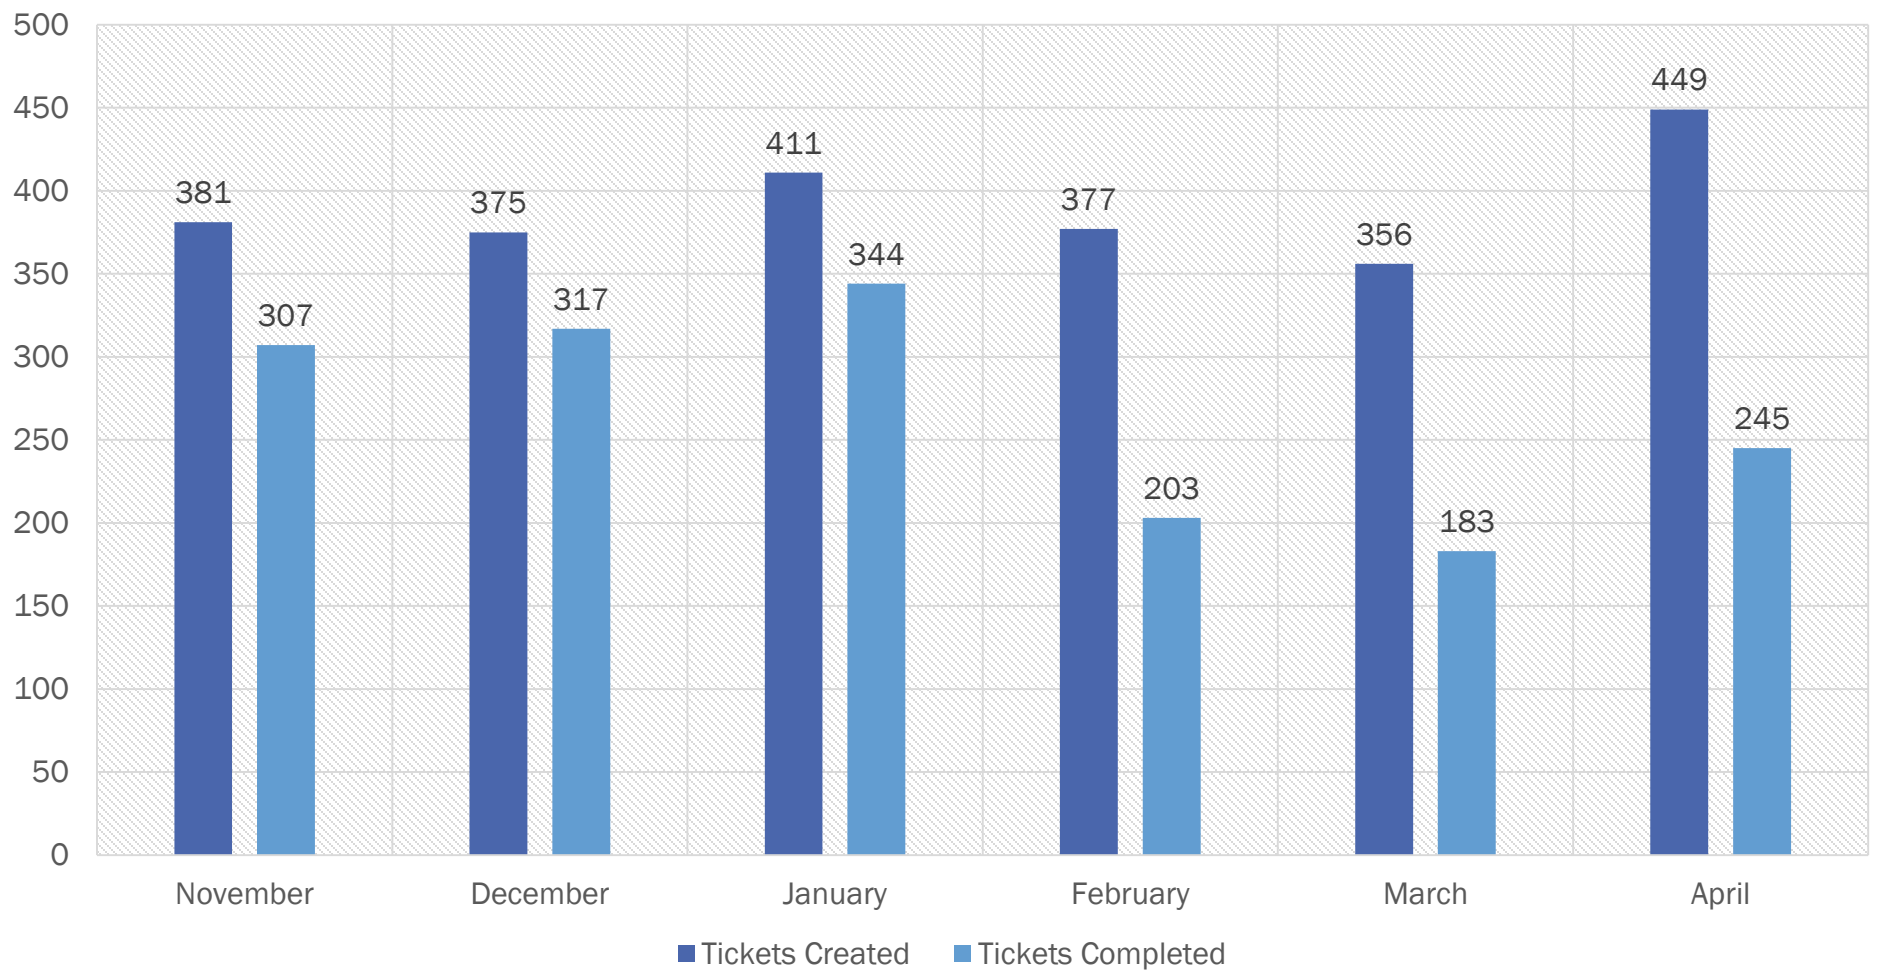

Created = 449
Closed = 245
Within 30 Days = 204
60 Days = 31
90 + Days = 20

Security
Created = 22
Open = 14
Closed = 8

SFDR Facility & Construction Report

Questions?

