

# Facilities & Construction Report

**PROJECT STATUS 12/18/2017**

- **New Construction**
  - Laughlin Elementary STEM Magnet School
  
- **Technology**
  - Service Desk - Monthly Report
  
- **Maintenance**
  - Service Desk - Monthly Report
  - Campus Upgrades
    - San Felipe Memorial Middle – Field Improvements
    - Playground Installations

# New Construction


## Laughlin Elementary STEM Magnet School




- Advertise for RFCP – Completed
- Receive RFCP – Completed
- Build Status – Completed
- Visual Inspection of Units – Completed
- General Contractor Awarding – Completed
- Ground Breaking – 12/12/2017
- Modular Building Relocation – 1/15/2018
- Walkways, Ramps, & Utilities – 3/1/2018

# Technology


## Support Tickets 11-1-2017 thru 12-1-2017

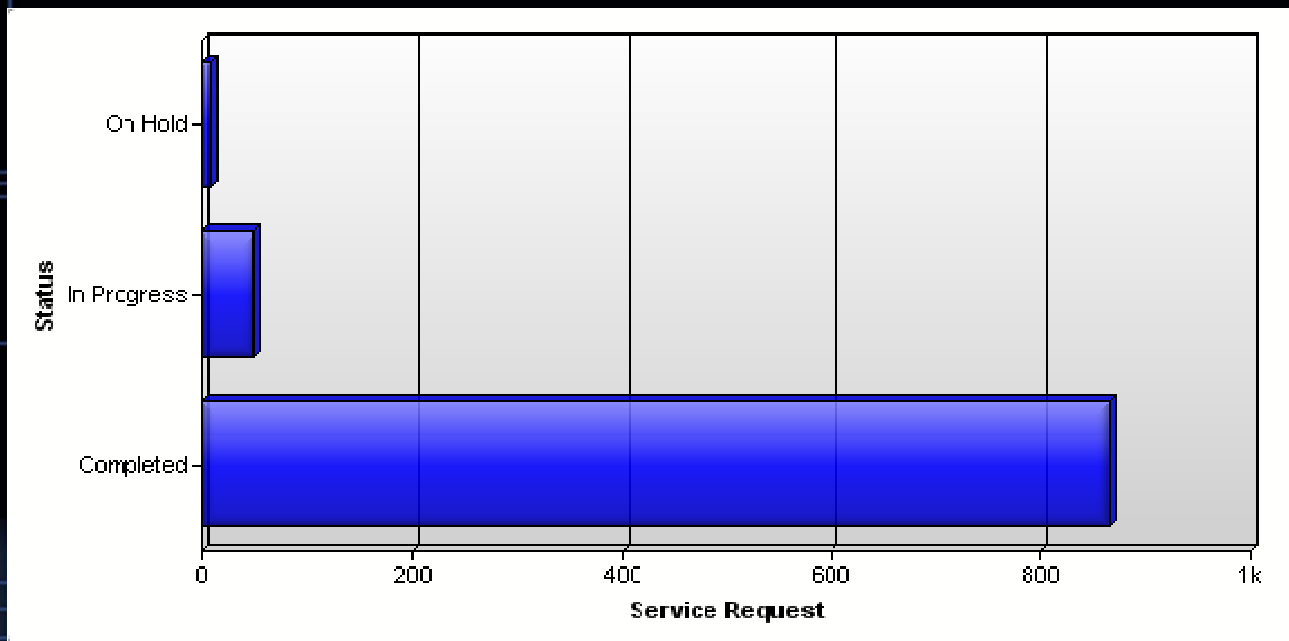

Tickets Submitted




Tickets Completed




Tickets Carried Over  
109

# Maintenance


## Support Tickets 11-1-2017 thru 12-1-2017

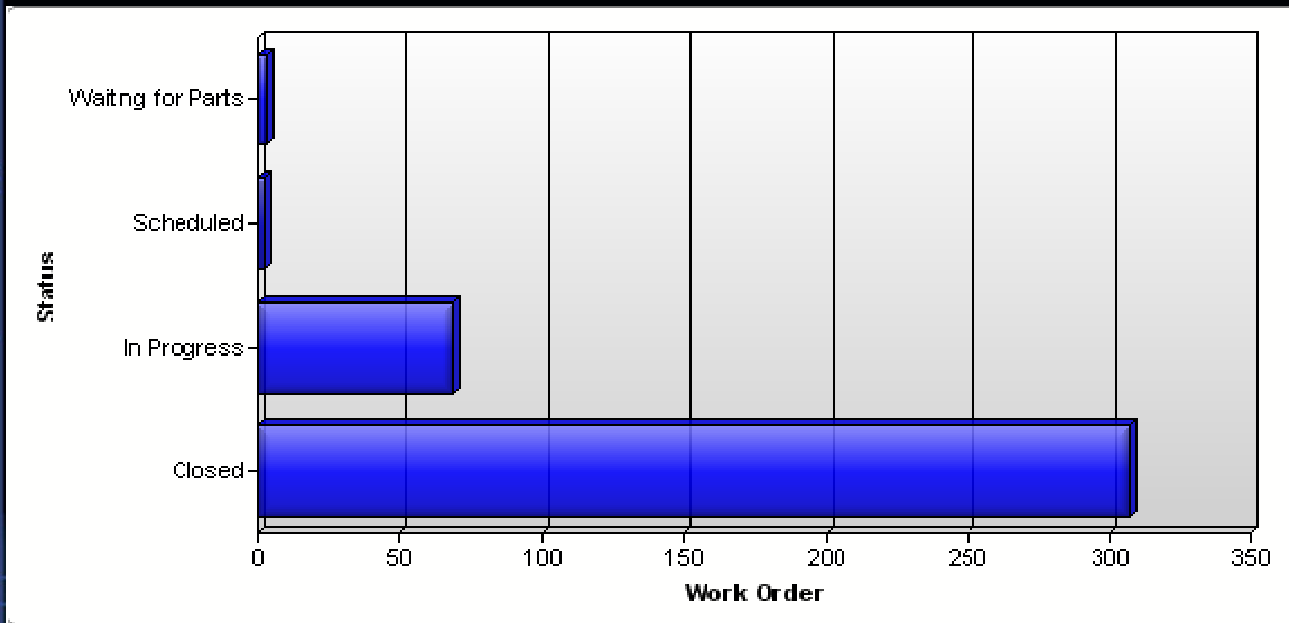

Tickets Submitted



Tickets Completed



Tickets Carried Over

74



# Maintenance – Campus Upgrades

## San Felipe Memorial Middle School – Field Improvements

Aluma goal All Purpose Backstop System  
21' High X 65" Wide



# Maintenance – Campus Upgrades

## Playground Installations

- Equipment Purchased from Laughlin AFB 2017
  - SFDR Cost = 10k
  - MSRP = 200K
- Deployment Status
  - Cardwell - Completed
  - Chavira - Completed
  - Calderon – In Progress
  - Del Rio Middle School – Design Phase
  - North Heights – Design Phase



The background is a dark blue gradient with a complex pattern of thin, light blue lines and shapes. On the left side, there are several vertical and horizontal lines forming a grid-like structure, with a circle partially overlapping them. On the right side, there are larger, semi-circular shapes and vertical lines. The overall aesthetic is technical and modern.

Questions?
